












ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 21, '07													
								W	T	F	S	S	M	T	W	T	F				
1		Advisor Meeting 1	1 hr	Thu 1/18/07	Thu 1/18/07		Kellen,Laura														
2		Group Meeting	1.5 hrs	Wed 1/24/07	Wed 1/24/07	1	Kellen,Laura														
3		Advisor Meeting 2	1.5 hrs	Thu 1/25/07	Thu 1/25/07	1	Kellen,Laura														
4		Project Meeting 1	0 hrs	Fri 1/26/07	Fri 1/26/07	1,2,3	Kellen,Laura														
5		Requirements Capture	1.5 days	Fri 1/26/07	Mon 1/29/07	4	Kellen,Laura														
6		Gantt Chart	1.5 days	Fri 1/26/07	Mon 1/29/07	4	Kellen,Laura														
7		Arrange Work Station	3 days	Mon 1/29/07	Wed 1/31/07		Dr. Glower														
8		Pick Motors	4 days	Mon 1/29/07	Thu 2/1/07		Laura														
9		Pick Raw Materials for testing (v	5 days	Mon 1/29/07	Fri 2/2/07		Laura														
10		Accessories (controller, display	8 days	Mon 1/29/07	Wed 2/7/07		Kellen														
11		Conceptual Design Document	6 days	Mon 2/5/07	Mon 2/12/07		Kellen,Laura														
12		Project Meeting 2	0 hrs	Fri 2/9/07	Fri 2/9/07	9,7,8,10	Kellen,Laura														
13		Order Motors/ Raw Materials	4 days	Mon 2/12/07	Thu 2/15/07	12	Laura														
14		Motor Testing	56 days	Tue 2/20/07	Tue 5/8/07	13	Laura														
15		Meet with Mechanical Departme	0 hrs	Tue 5/8/07	Tue 5/8/07	14	Kellen,Laura														
16		Abdomanol Motor Testing	56 days	Fri 2/16/07	Fri 5/4/07	13	Laura														
17		Software Design (Abdomen)	28 days	Thu 2/8/07	Mon 3/19/07	10	Kellen Nesvig														
18		Integrate with Control Unit	3 days	Mon 5/7/07	Wed 5/9/07	16,17	Kellen,Laura														
19		Progress Meeting/Advisor Review	0 hrs	Fri 3/9/07	Fri 3/9/07		Kellen,Laura														
20		Troubleshooting	21 days	Thu 5/10/07	Thu 6/7/07	18	Kellen,Laura														
21		Meet with Mechanical Departme	0 hrs	Thu 6/7/07	Thu 6/7/07	20	Kellen,Laura														
22		Arms Motor Testing	56 days	Fri 6/8/07	Fri 8/24/07	21	Laura														
23		Software Design (Arms)	14 days	Fri 6/8/07	Wed 6/27/07	21	Kellen Nesvig														
24		Integrate with Control Unit	3 days	Mon 8/27/07	Wed 8/29/07	22,23	Kellen,Laura														
25		Troubleshooting	21 days	Thu 8/30/07	Thu 9/27/07	24	Kellen,Laura														
26		Meet with Mechanical Departme	0 hrs	Thu 9/27/07	Thu 9/27/07	25	Kellen,Laura														
27		Legs Motor Testing	56 days	Fri 9/28/07	Fri 12/14/07	26	Laura														
28		Software Design (Legs)	7 days	Fri 9/28/07	Mon 10/8/07	26	Kellen Nesvig														
29		Integrate with Control unit	3 days	Mon 12/17/07	Wed 12/19/07	27,28	Kellen,Laura														
30		Troubleshooting	21 days	Thu 12/20/07	Thu 1/17/08	29	Kellen,Laura														
31		Convert Testing Model to Protocol	90 days	Fri 1/18/08	Thu 5/22/08	30															
32		SBIR Proposal	18 days	Mon 10/29/07	Wed 11/21/07		Kellen,Laura														



Project: Exercise Chair2 Date: Thu 3/29/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

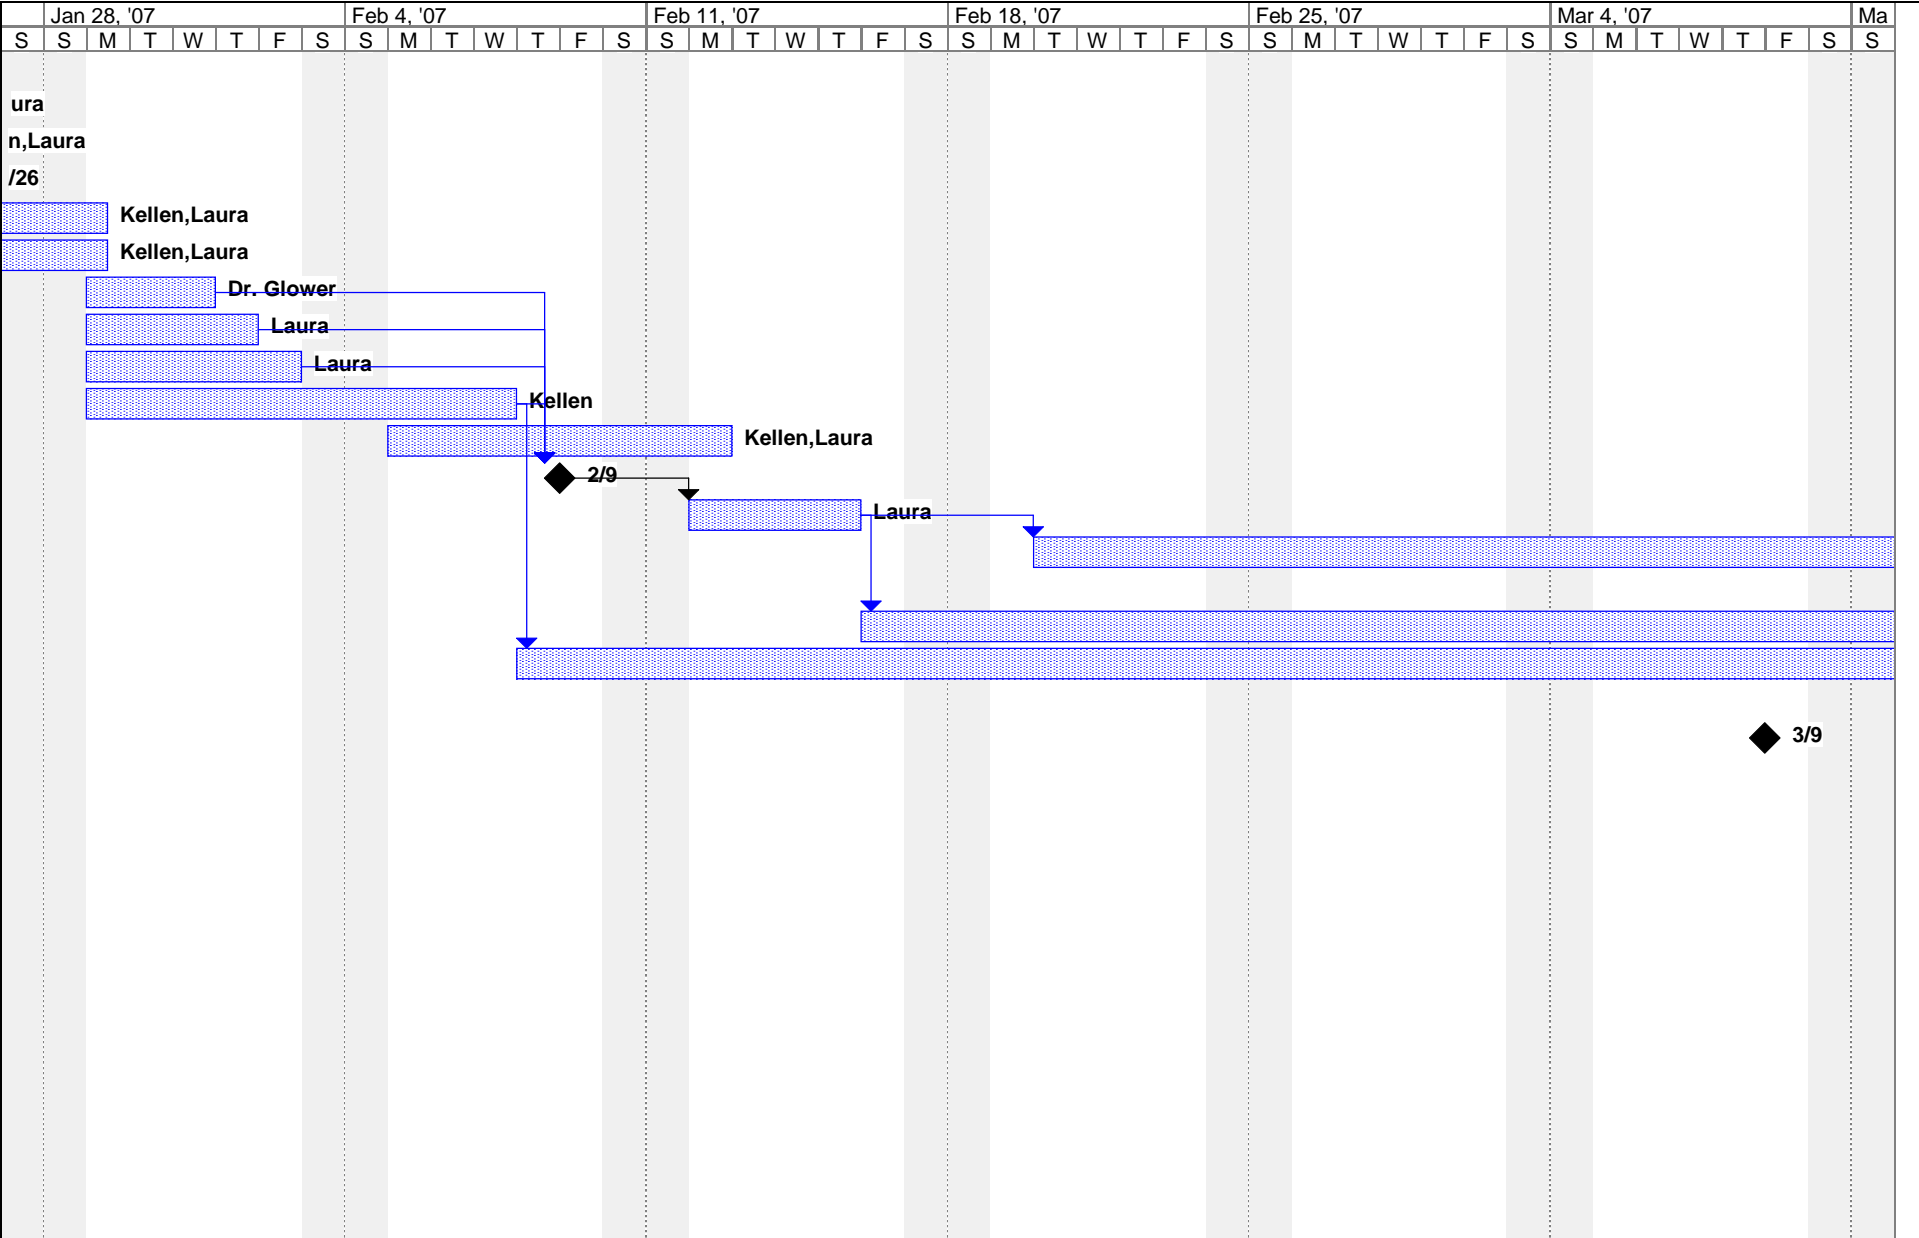

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

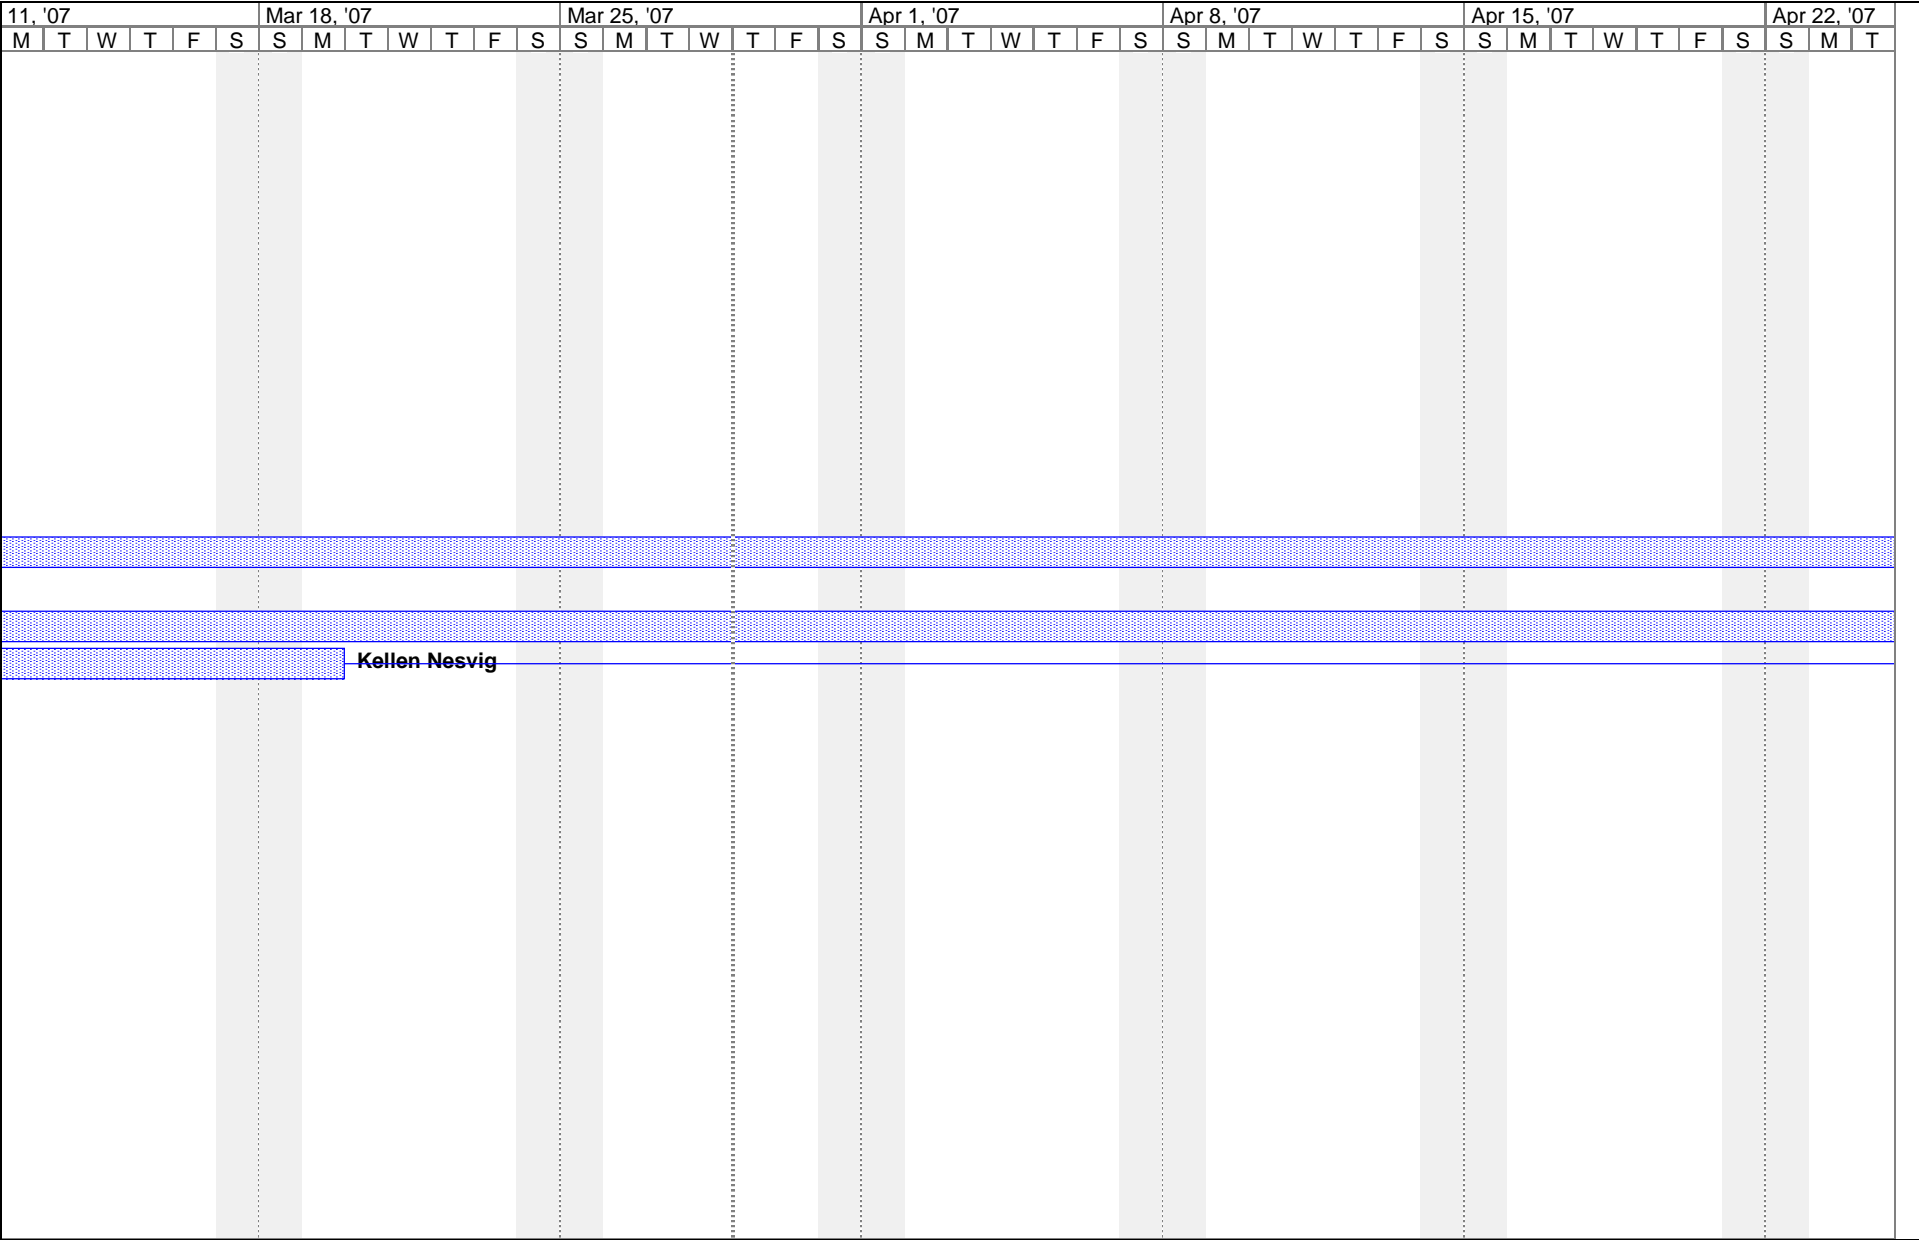

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

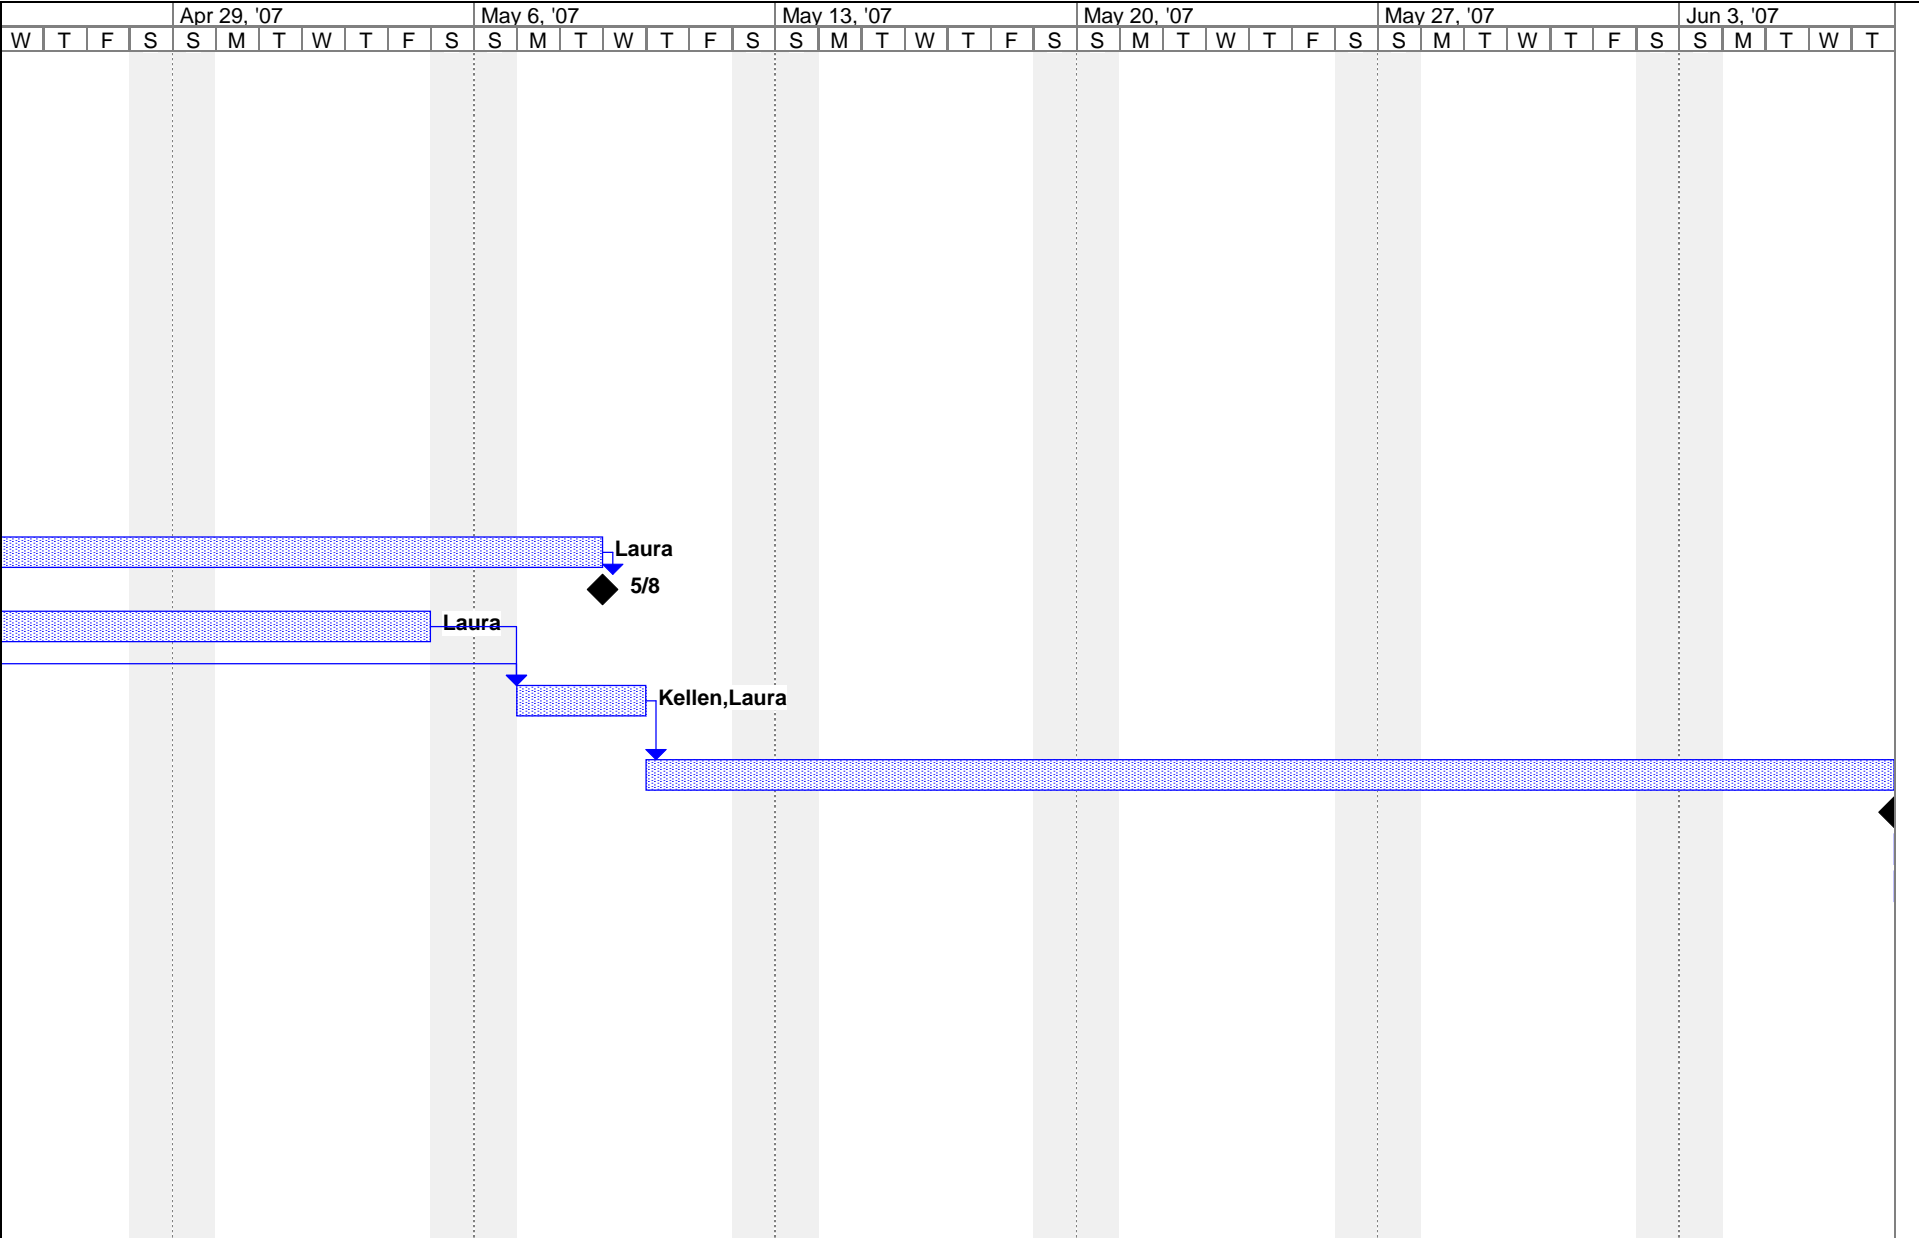

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress







Milestone

Summary

Project Summary







External Tasks


External Milestone

Deadline







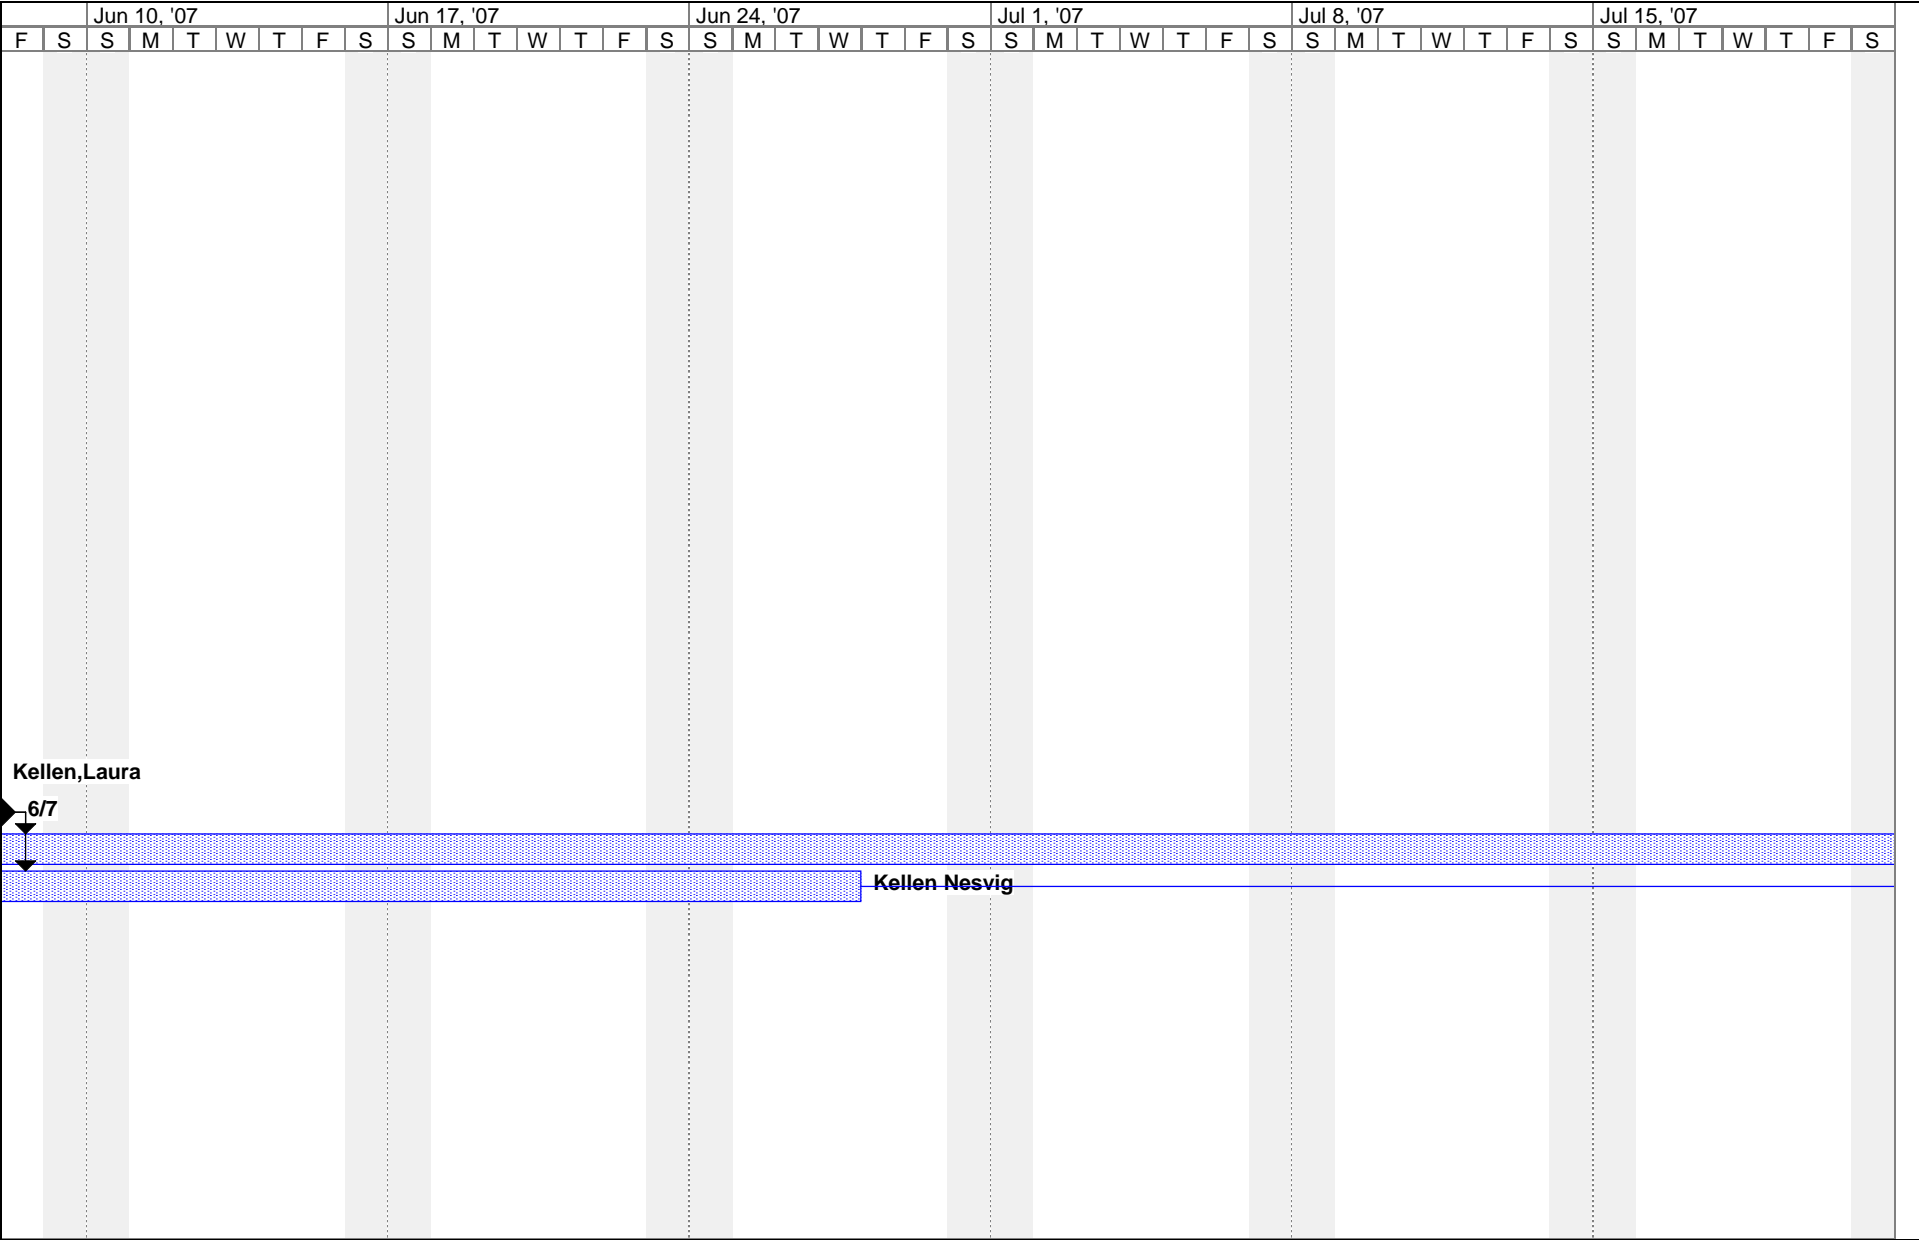

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

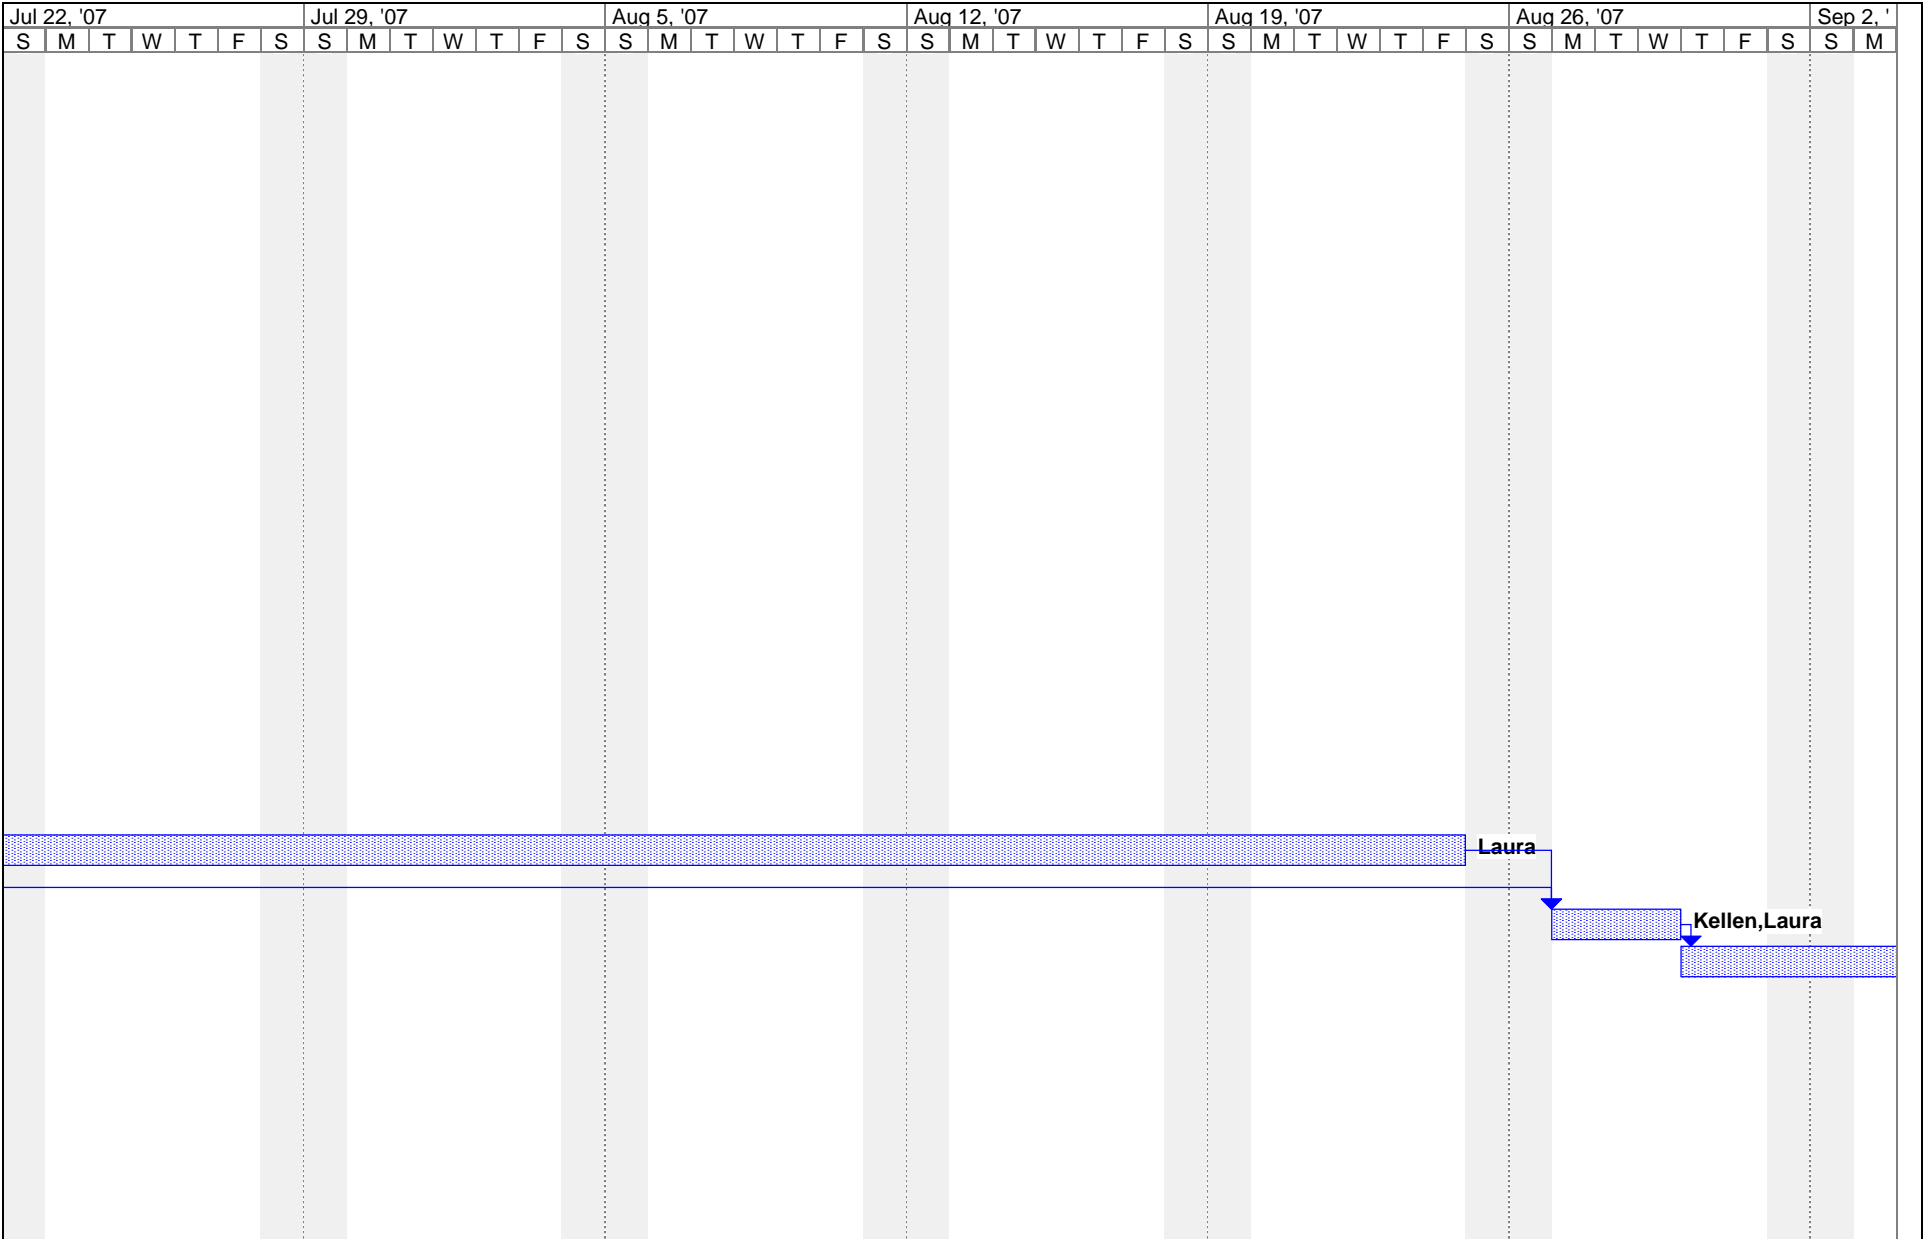

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

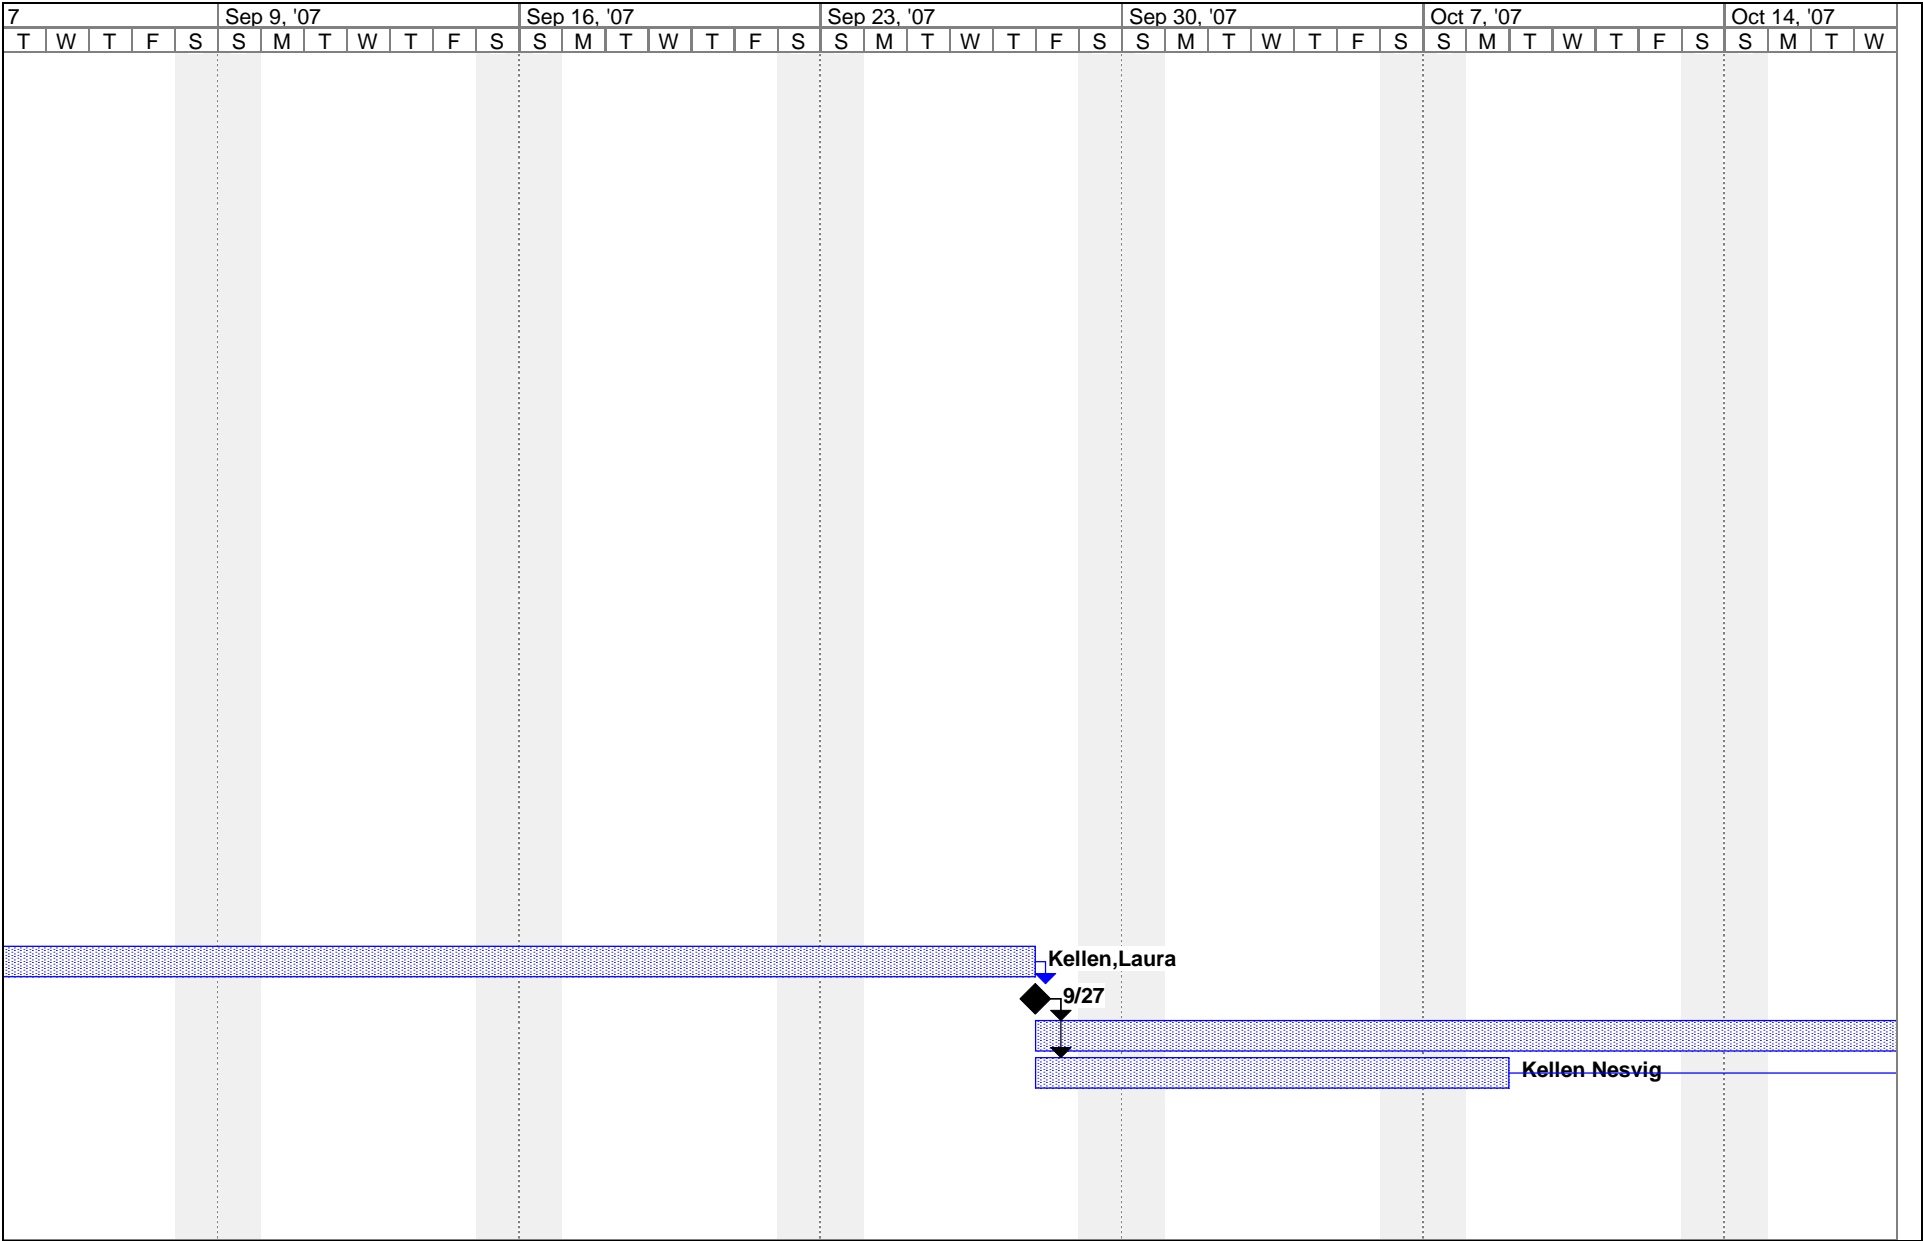

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress







Milestone

Summary

Project Summary







External Tasks

External Milestone

Deadline








[illegible]

Project: Exercise Chair2  
Date: Thu 3/29/07

## Task



## Milestone



## External Tasks



Split



## Summary



### External Milestone



## Progress




## Project Summary



Deadline





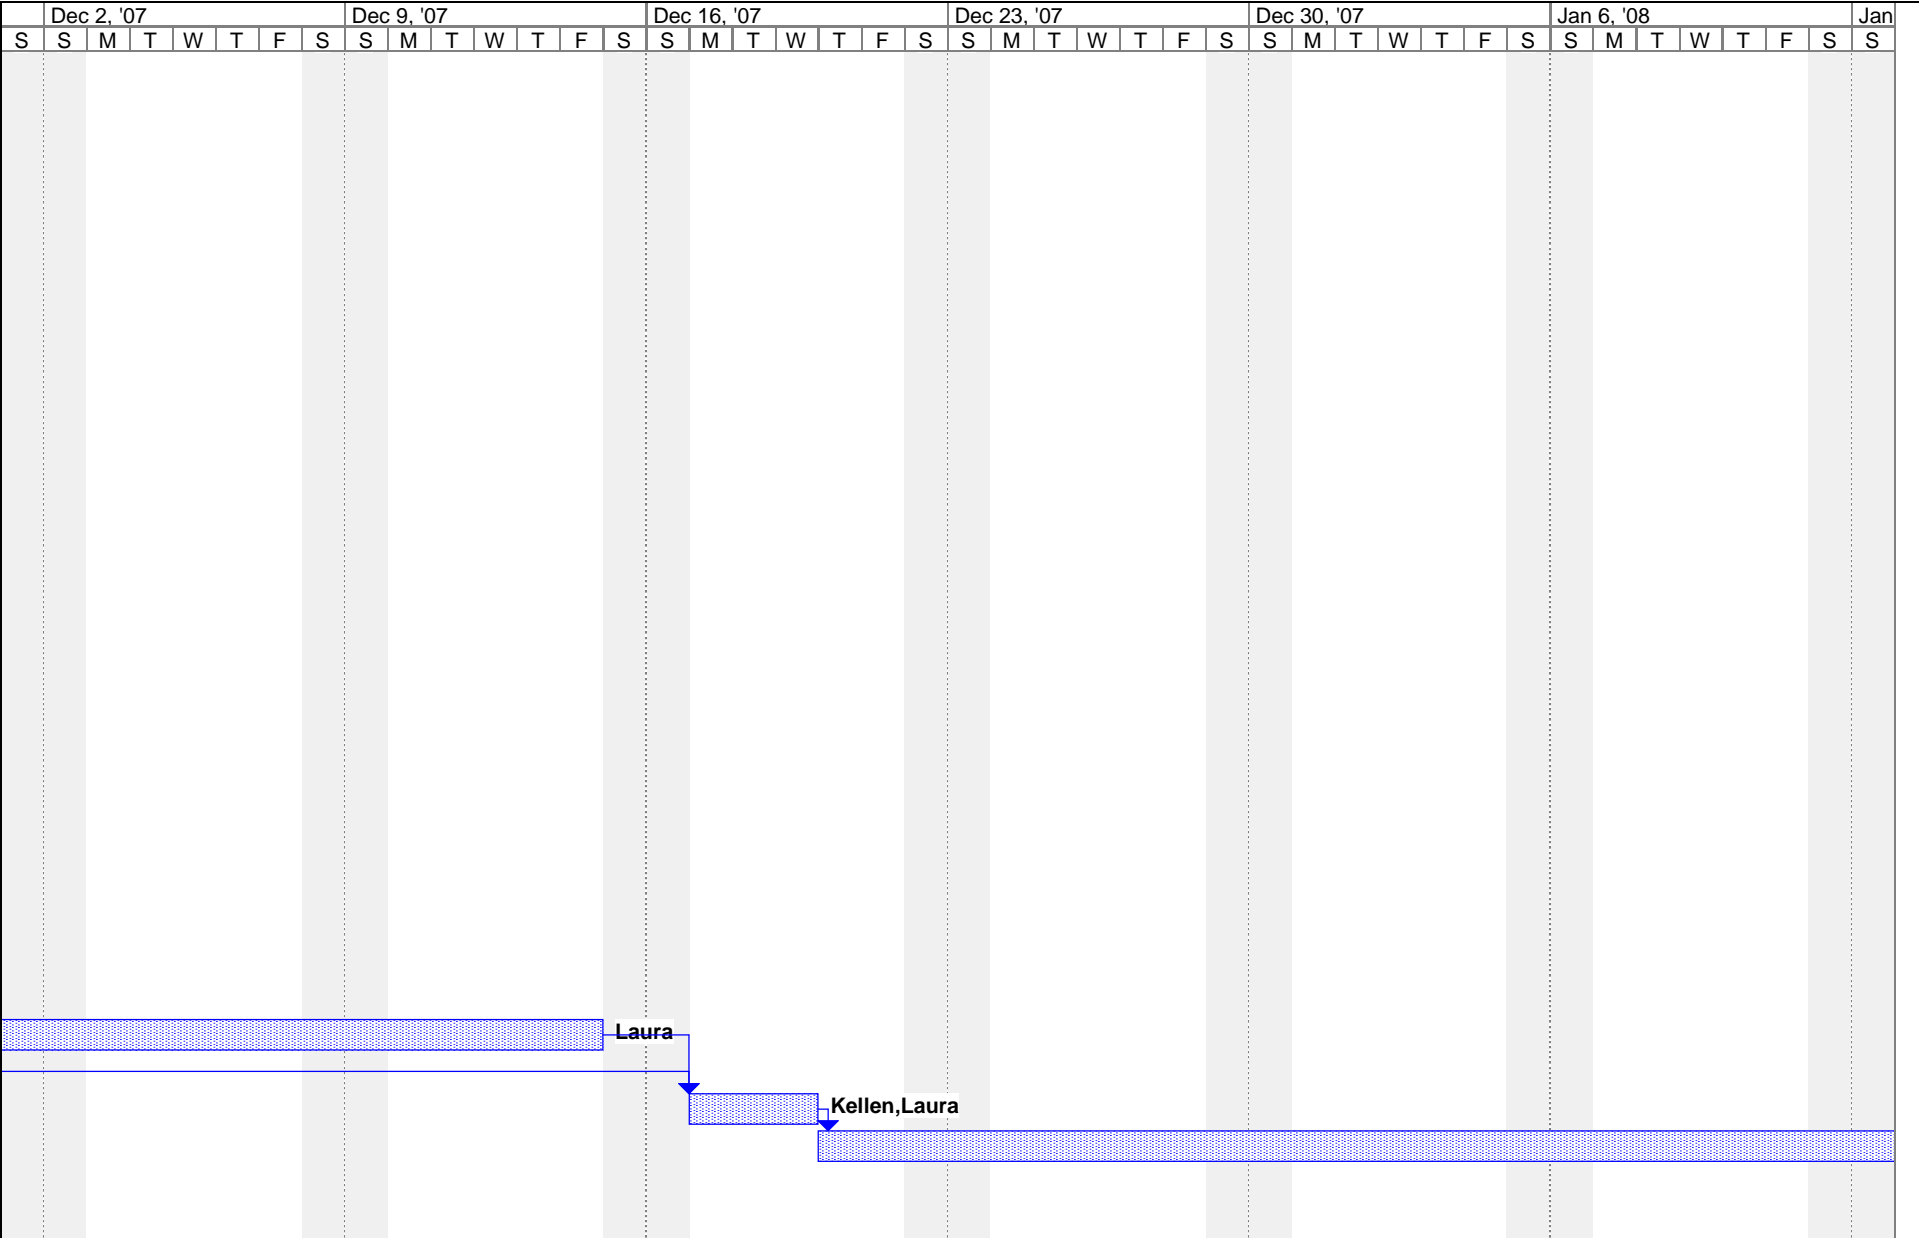

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks


External Milestone

Deadline

13, '08							Jan 20, '08							Jan 27, '08							Feb 3, '08							Feb 10, '08							Feb 17, '08							Feb 24, '08		
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T								

Project: Exercise Chair2  
Date: Thu 3/29/07

## Task



## Milestone



## External Tasks



Split



## Summary



### External Milestone



## Progress




## Project Summary



Deadline



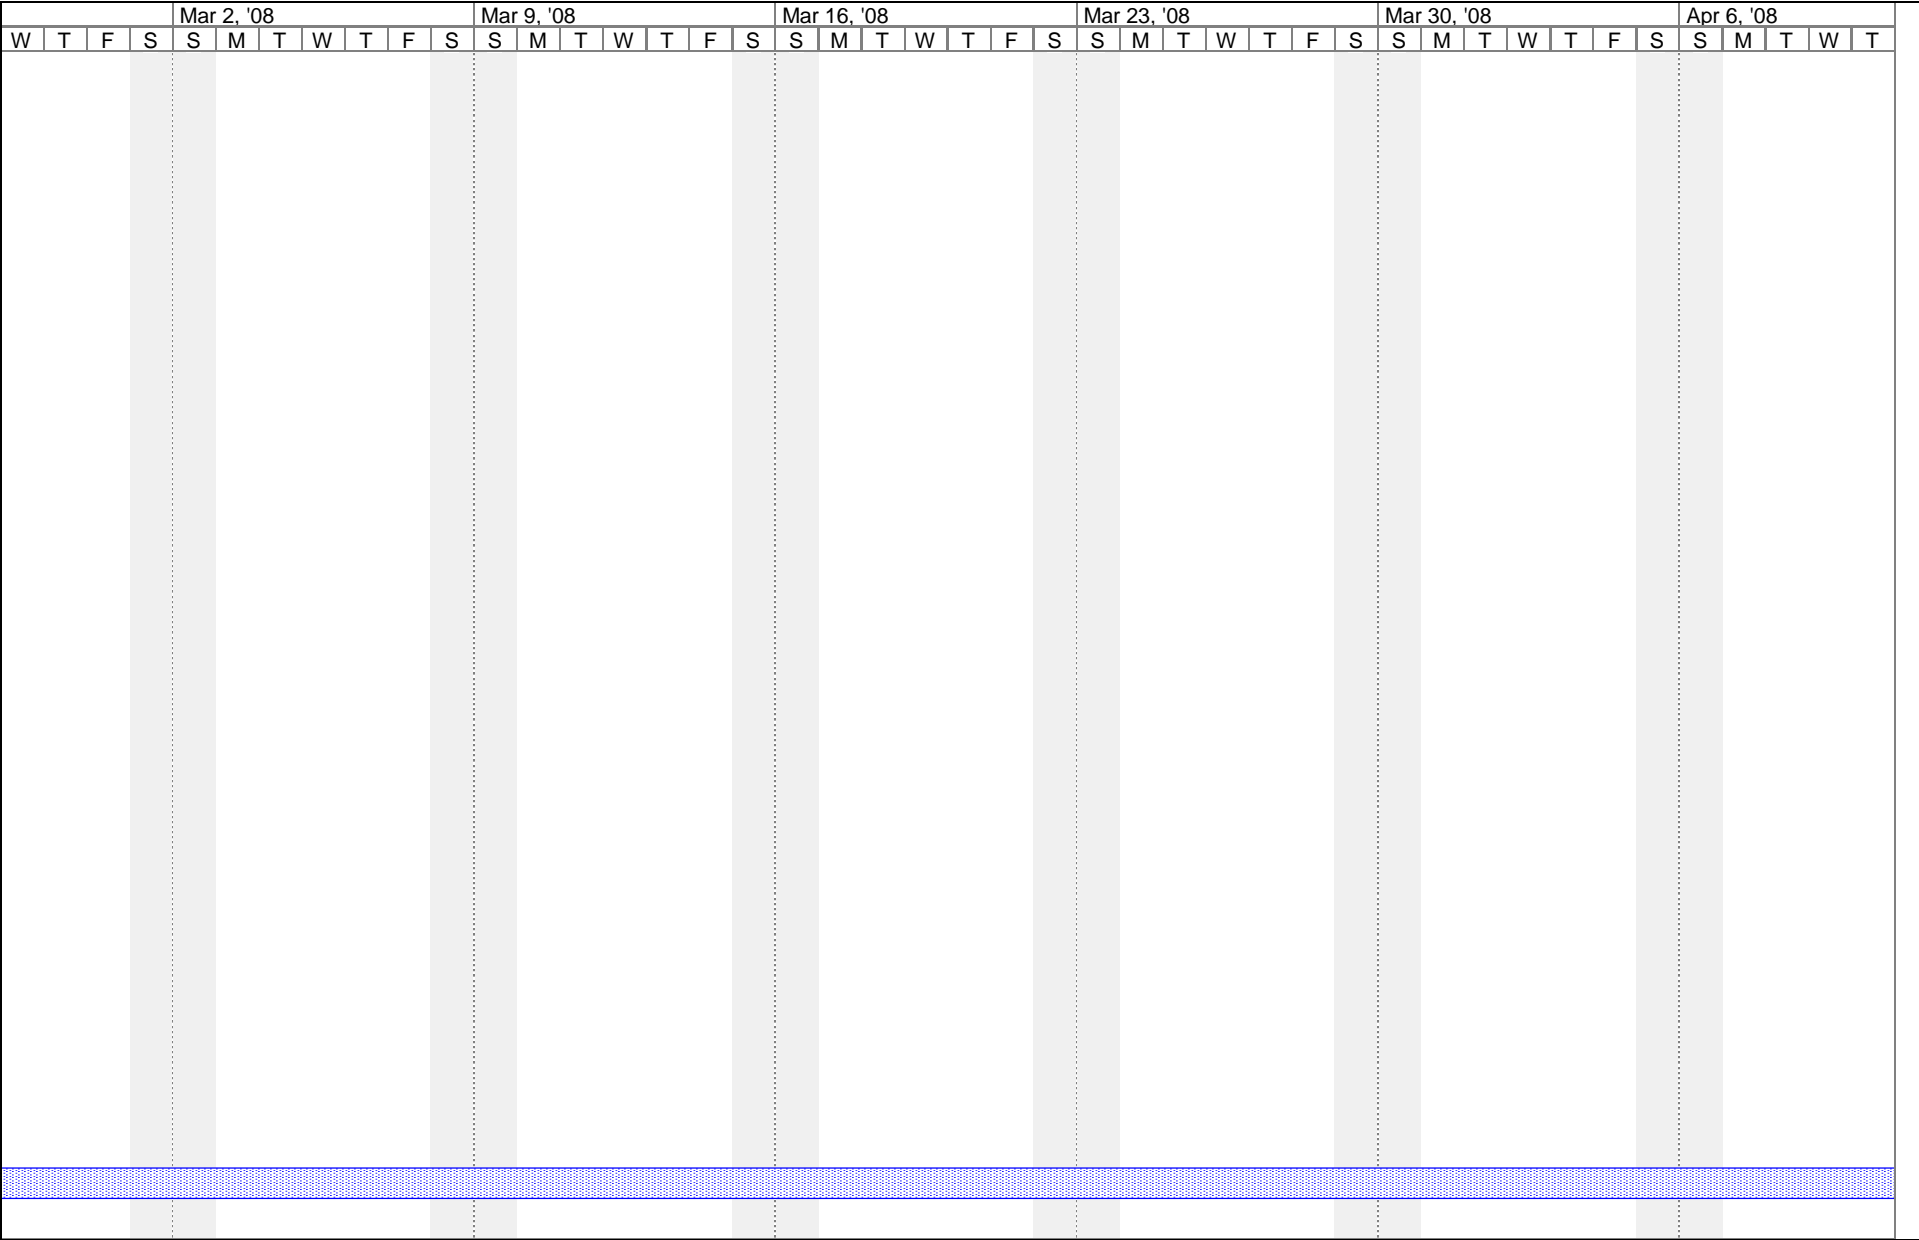

Project: Exercise Chair2  
Date: Thu 3/29/07

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

[illegible]
